



ID	Task Mode	Task Name	Duration	Start	Finish	'21	Sep 19, '21	Oct 17, '21	Nov 14, '21	Dec 12, '21	Jan 9, '22	Feb 6, '22	Mar 6, '22	Apr 3, '22	M
						S	W	S	T	M	F	T	S	W	
0		West Orange Flood & Drainage Improvements	142 days	Mon 9/27/21	Tue 4/12/22										
1	✓	Phase 1	35 days	Mon 9/27/21	Fri 11/12/21										
2	✓	Mobilization	2 days	Mon 9/27/21	Tue 9/28/21										
3	✓	Bowie Ave	7 days	Wed 9/29/21	Thu 10/7/21										
4	✓	Milam Ave	12 days	Fri 10/8/21	Mon 10/25/21										
5	✓	Dowling Ave	12 days	Tue 10/26/21	Wed 11/10/21										
6	✓	Jasper Ave	2 days	Thu 11/11/21	Fri 11/12/21										
7		Phase 2	45 days	Mon 11/15/21	Fri 1/14/22										
8		Dayton St	20 days	Mon 11/15/21	Fri 12/10/21										
9		Western Ave	10 days	Thu 11/25/21	Wed 12/8/21										
10		South Ave Phase 1	9 days	Mon 12/13/21	Thu 12/23/21										
11		Winter Break	7 days	Fri 12/24/21	Mon 1/3/22										
12		South Ave Pahse 2	9 days	Tue 1/4/22	Fri 1/14/22										
13		Phase 3	34 days	Mon 1/17/22	Thu 3/3/22										
14		Davis Ave	5 days	Mon 1/17/22	Fri 1/21/22										
15		Bradford St	13 days	Mon 1/24/22	Wed 2/9/22										
16		Holly St	5 days	Thu 2/10/22	Wed 2/16/22										
17		Crabtree St	5 days	Thu 2/17/22	Wed 2/23/22										
18		Mulberry St	3 days	Thu 2/24/22	Mon 2/28/22										
19		Plum St	3 days	Tue 3/1/22	Thu 3/3/22										
20		Phase 4	31 days	Tue 3/1/22	Tue 4/12/22										
21		Linda St	3 days	Fri 3/4/22	Tue 3/8/22										
22		Katherine St	3 days	Wed 3/9/22	Fri 3/11/22										
23		Joyce St	3 days	Mon 3/14/22	Wed 3/16/22										
24		Irene St	3 days	Thu 3/17/22	Mon 3/21/22										
25		Henrietta St	7 days	Tue 3/22/22	Wed 3/30/22										
26		Gloria St	3 days	Thu 3/31/22	Mon 4/4/22										
27		Tanglewood West	3 days	Tue 4/5/22	Thu 4/7/22										
28		Ester St	5 days	Tue 3/1/22	Mon 3/7/22										
29		Donnell St	5 days	Tue 3/8/22	Mon 3/14/22										
30		Carol St	5 days	Tue 3/15/22	Mon 3/21/22										
31		Broad St	5 days	Tue 3/22/22	Mon 3/28/22										
32		Alder St	2 days	Tue 3/29/22	Wed 3/30/22										

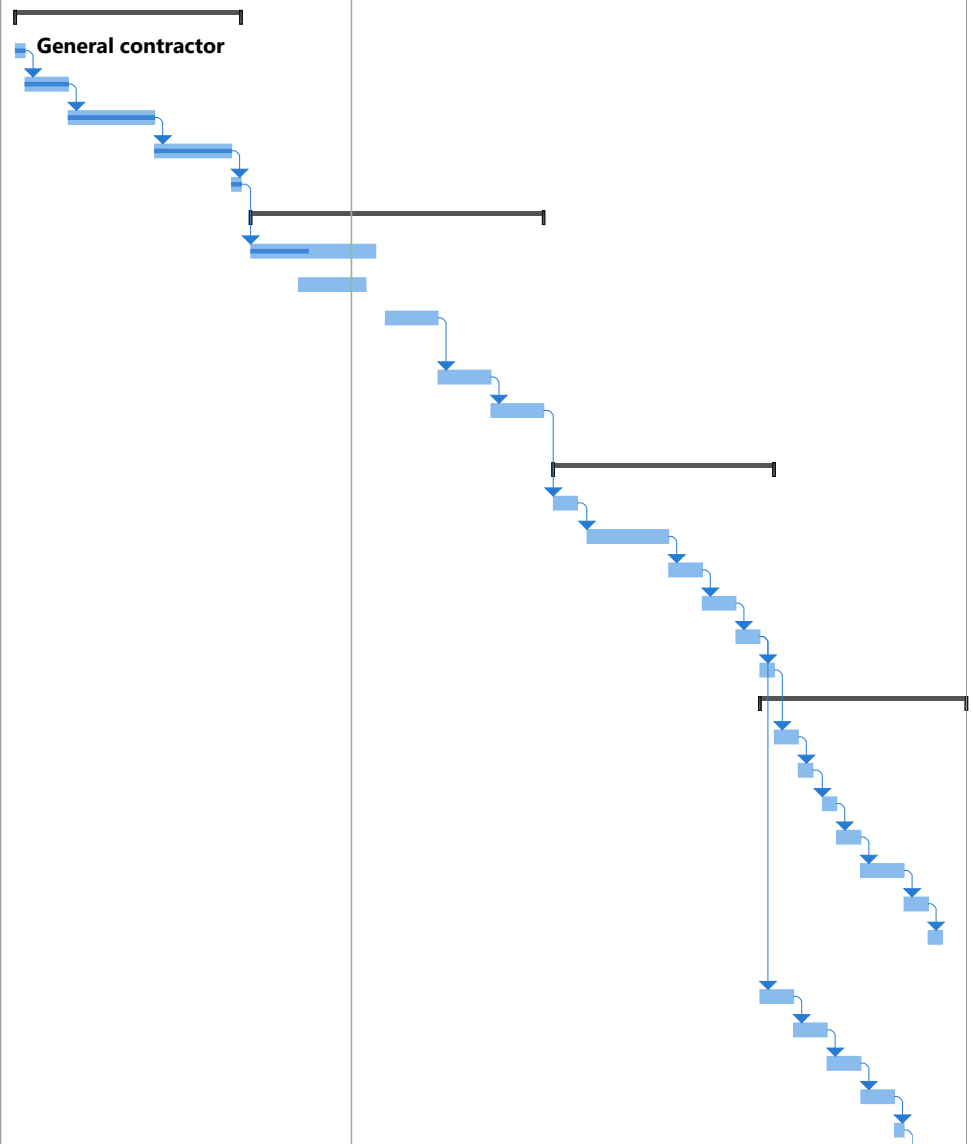

Project: West Orange Flood & Drainage Improvements
Date: Mon 12/6/21

Task		Inactive Task		Manual Summary Rollup		External Milestone	
Split		Inactive Milestone		Manual Summary		Deadline	
Milestone		Inactive Summary		Start-only		Progress	
Summary		Manual Task		Finish-only		Manual Progress	
Project Summary		Duration-only		External Tasks			

ID		Task Mode	Task Name	Duration	Start	Finish																												
							'21 S	W	Sep 19, '21 S	T	Oct 17, '21 M	F	T	Nov 14, '21 S	W	Dec 12, '21 S	T	M	F	T	Jan 9, '22 S	W	S	T	M	F	T	S	Feb 6, '22 S	W	S	T	M	F
33			Stakes St	5 days	Thu 3/31/22	Wed 4/6/22																												
34			Tanglewood East	4 days	Thu 4/7/22	Tue 4/12/22																												



Project: West Orange Flood & Date: Mon 12/6/21	Task		Inactive Task		Manual Summary Rollup		External Milestone	
	Split		Inactive Milestone		Manual Summary		Deadline	
	Milestone		Inactive Summary		Start-only		Progress	
	Summary		Manual Task		Finish-only		Manual Progress	
	Project Summary		Duration-only		External Tasks			
